

Burlington Fox Hill Elementary School Project

School Building Committee Meeting #40
April 8th , 6:00 PM



SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn

Amendments

Dore & Whittier Amendment No. 6 in the amount of \$31,900 for DD estimating

Invoices

- DiNisco Invoice No. 10184 in the amount of \$ 356,444 for Construction Documents 1 of 9
- DiNisco Invoice No. 10185 in the amount of \$3,343.45 for Traffic Studies
- DiNisco Invoice No. 10186 in the amount of \$2,360.88 for Wetlands Design Development and NOI
- DiNisco Invoice No. 10187 in the amount of \$6,810.65 for Additional Survey
- Dore and Whittier Invoice No. 31 in the amount of \$ 22,730 for Design Development

SBC Meeting Agenda – April 8th 2025

Budget Revision Request (BRR) Dore & Whittier Budget Revision No. 2.

From Classifi- cation Code	From Classification Name	To Classifi- cation Code	To Classification Name	Budget Revision Amount	Reason for transfer	Amount Remaining in Revised Budget Line
0201-0700	A&E - Construction Contract Administration	0201-0400	A&E - Design Development	\$183,000.00	Transfer to realign budget with executive contracts	\$43,950.00
0201-0700	A&E - Construction Contract Administration	0201-0500	A&E- Construction Contract Documents	\$34,000.00	Transfer to realign budget with executive contracts	\$9,950.00
0201-0700	A&E - Construction Contract Administration	0201-0600	A&E - Bidding	\$2,600.00	Transfer to realign budget with executive contracts	\$7,350.00
0201-0700	A&E - Construction Contract Administration	0201-0800	A&E - Closeout	\$400.00	Transfer to realign budget with executive contracts	\$6,950.00
0201-0700	A&E - Construction Contract Administration	0204-0300	A&E - Geotech & Geotech Environment	\$6,540.90	Transfer to realign budget with executive contracts	\$409.10

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn




School Building
Committee
Meeting

BURLINGTON ELEMENTARY SCHOOL

Burlington, MA

Project Schedule | Detailed Timeline

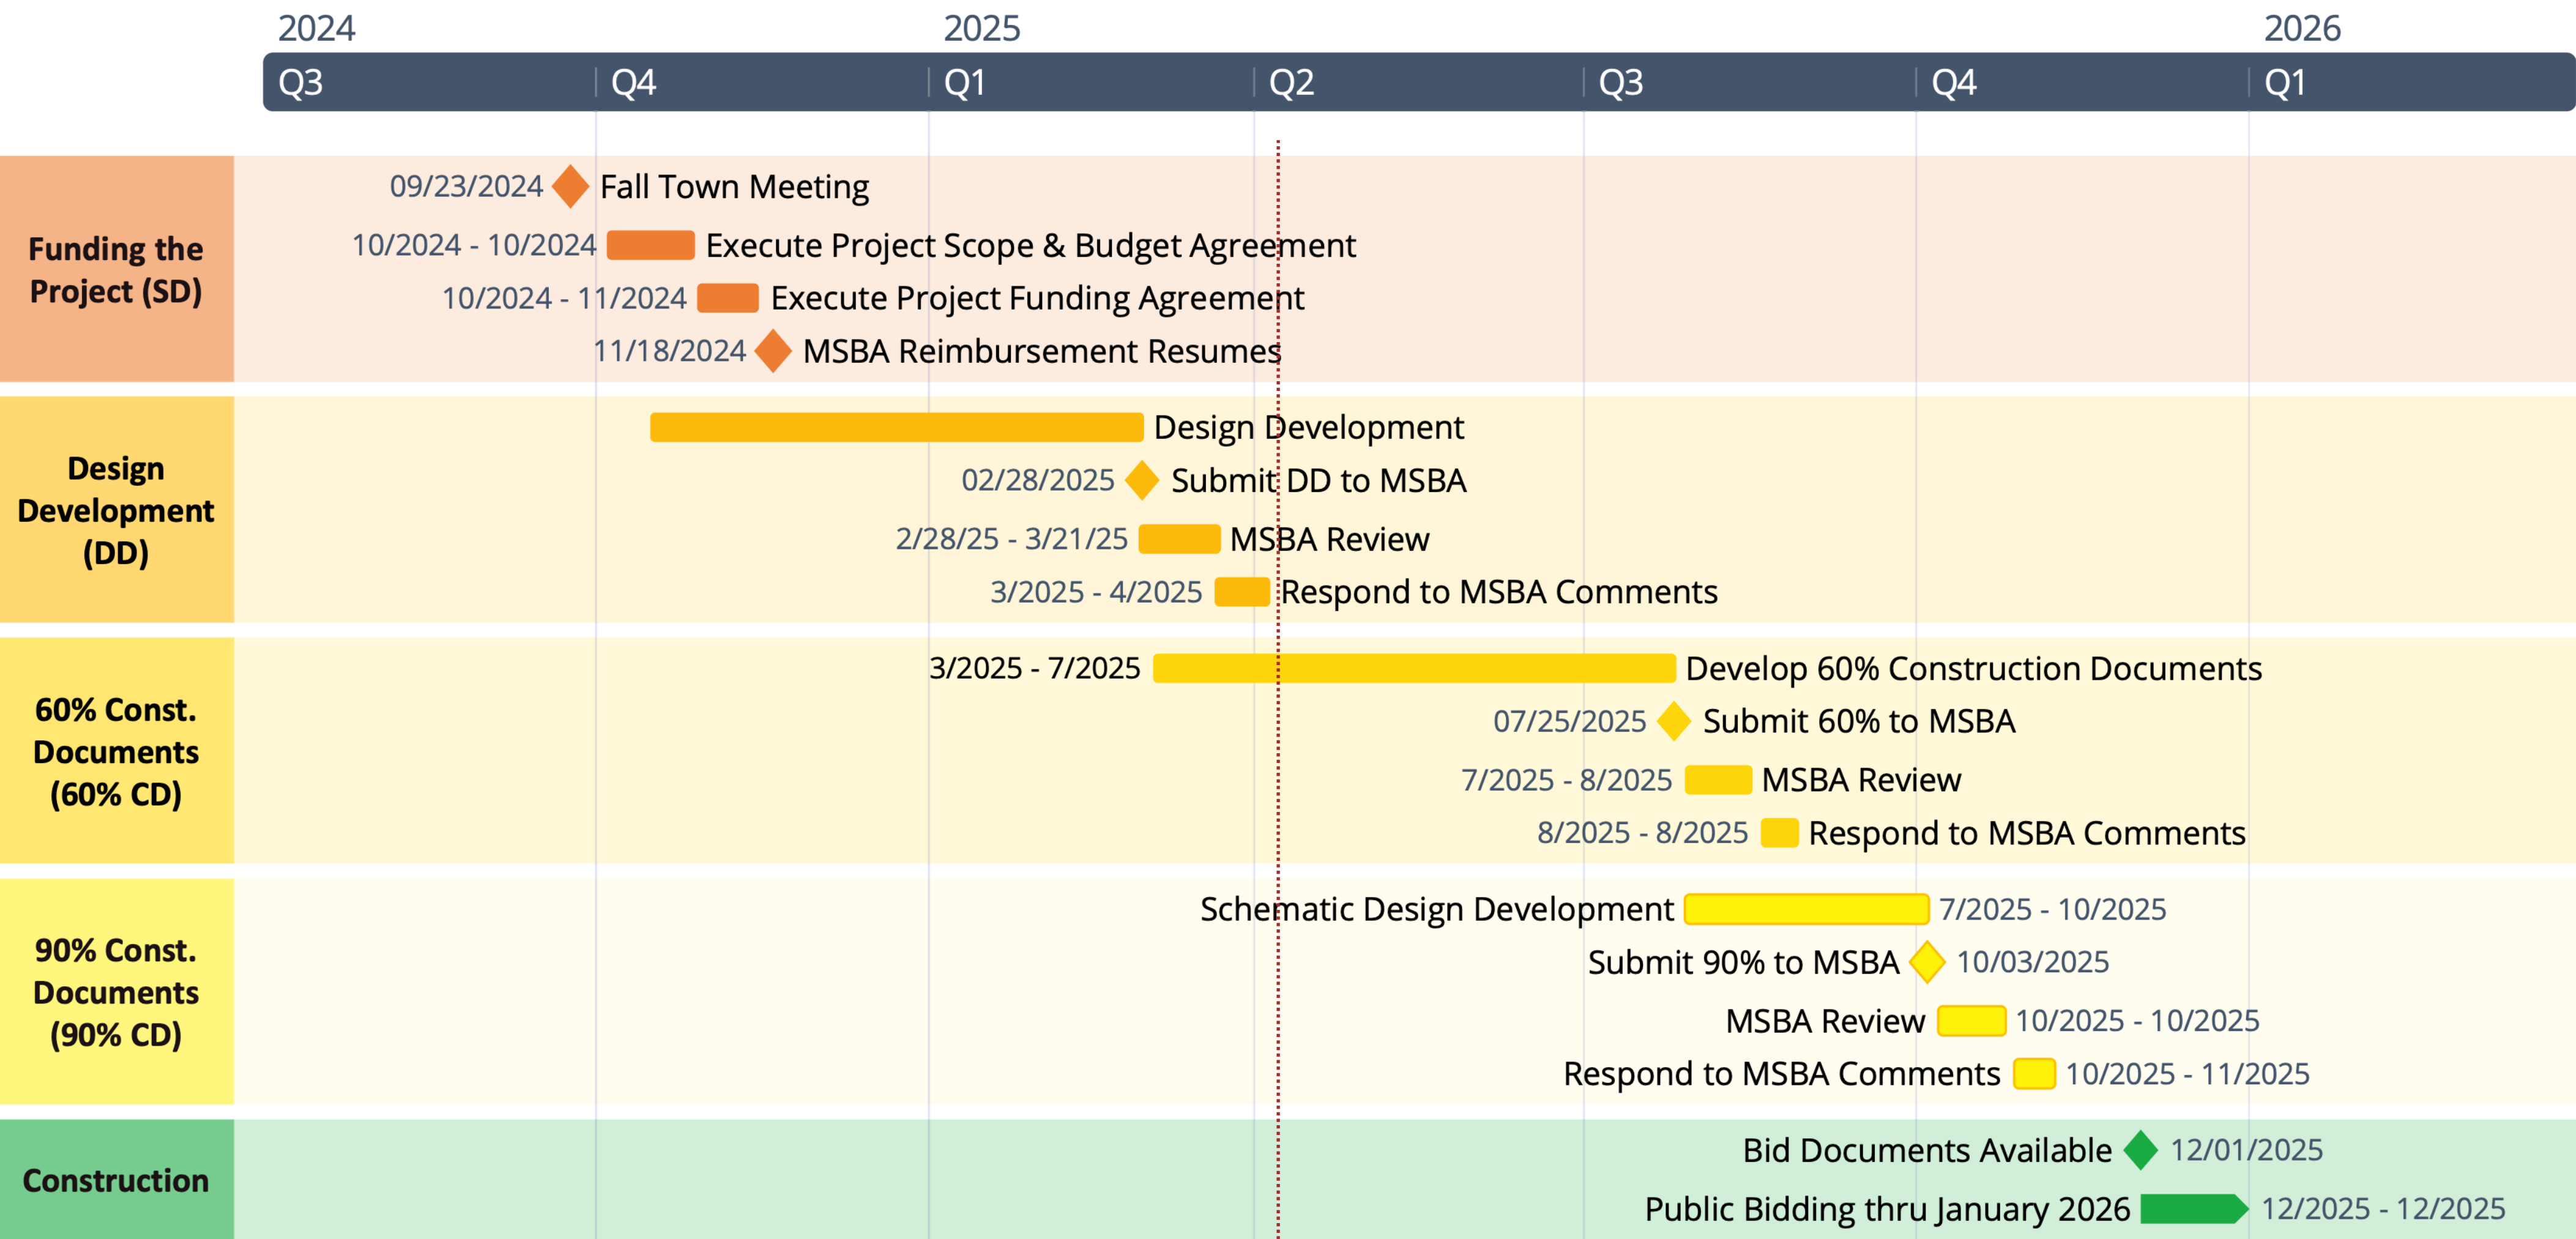



Interior Concepts | Celebrating Nature and All the Ways We Learn

Each area will feature local nature scenes and celebrate students' differences and the different ways that they learn.

Discover
CORRIDOR
Wetlands

**Play, Read,
& Create**
MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond

Explore
STAIR A
Local & New England
Trails and Parks

Search
CENTRAL STAIR
Sawmill Brook

Interior Concepts | West Entry Stair A - Bus Drop Off

Each area will feature local nature scenes and celebrate students' differences and the different ways that they learn.

Discover
CORRIDOR
Wetlands

**Play, Read,
& Create**

MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond

Explore


STAIR A
Local & New England
Trails and Parks

Search

CENTRAL STAIR
Sawmill Brook

Building Interior | West Entry Stair A - Bus Drop Off

Explore
STAIR A
Local Trails and Rivers

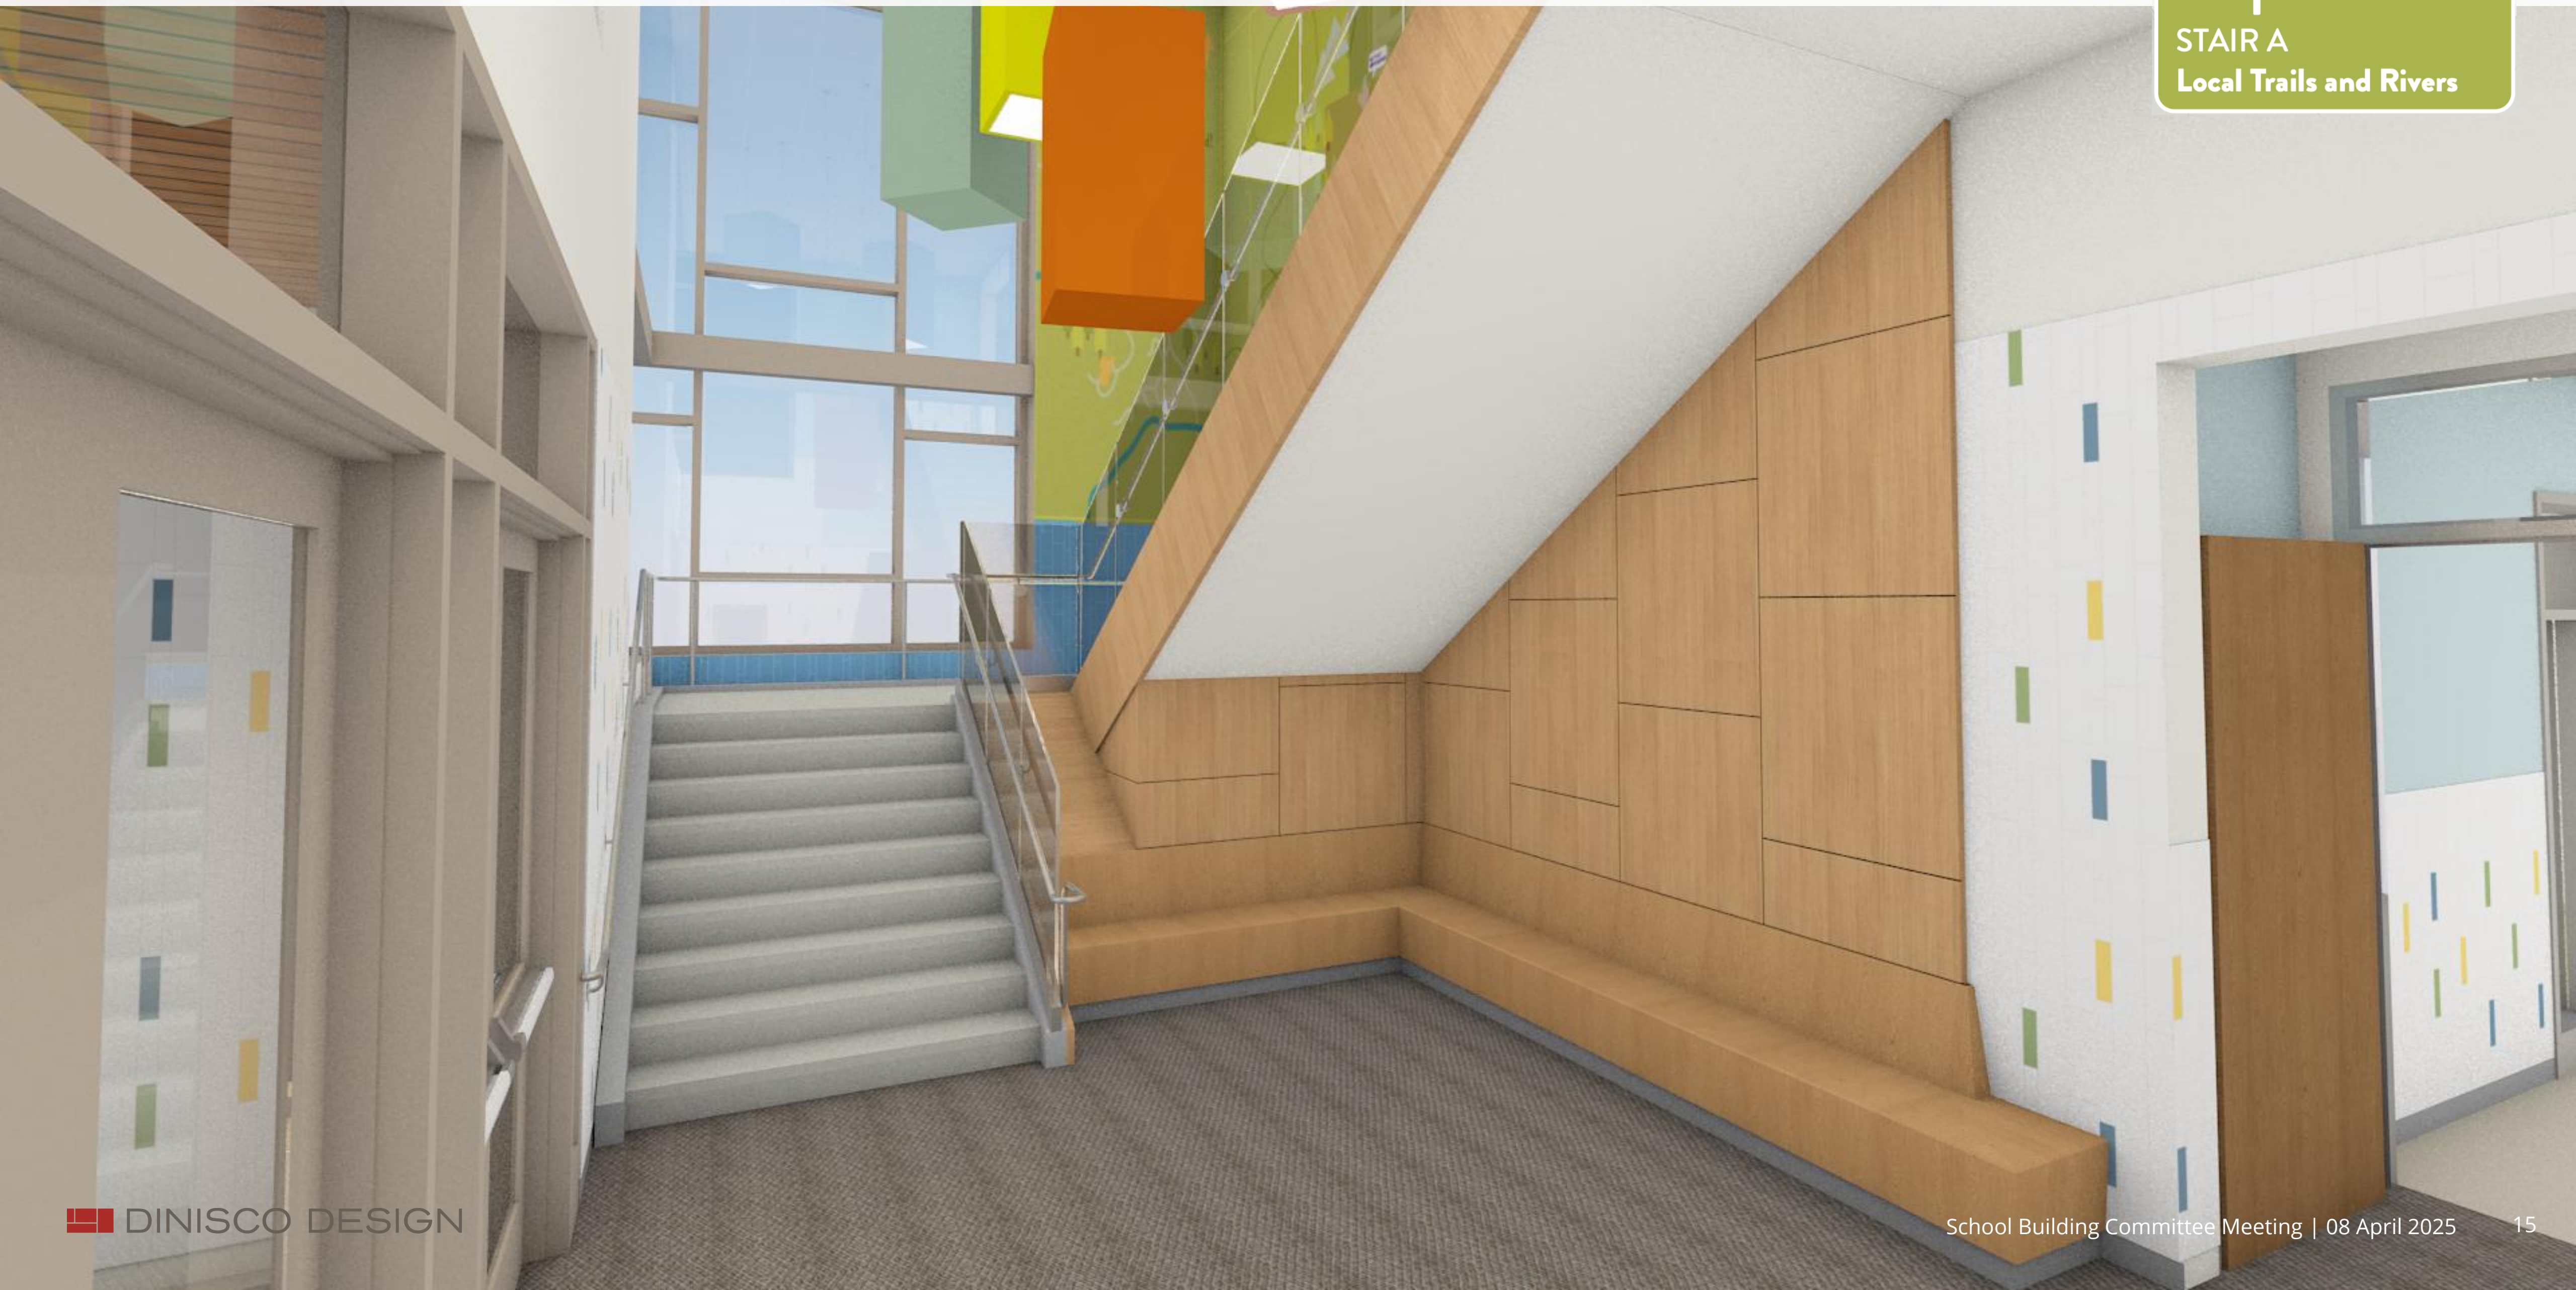

Building Interior | West Entry Stair A - Bus Drop Off

Explore

STAIR A
Local Trails and Rivers



Interior Concepts | Stair B - Academic Wing

Each area will feature local nature scenes and celebrate students' differences and the different ways that they learn.

Discover
CORRIDOR
Wetlands

Play, Read,
& Create
MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond

Explore
STAIR A
Local & New England
Trails and Parks

Search
CENTRAL STAIR
Sawmill Brook

Building Interior | Stair B - Academic Wing

Search
CENTRAL STAIR
Mill Pond/Sawmill Brook



Building Interior | Stair B - Academic Wing

Search

CENTRAL STAIR
Mill Pond/Sawmill Brook



Interior Concepts | Lobby - Corridor to Outdoor Classroom

Each area will feature local nature scenes and celebrate students' differences and the different ways that they learn.

Discover
CORRIDOR
Wetlands

**Play, Read,
& Create**
MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond

Explore
STAIR A
Local & New England
Trails and Parks

Search
CENTRAL STAIR
Sawmill Brook

Building Interior | Lobby View Towards Outdoor Classroom

Discover

CORRIDOR
Wetlands



Building Interior | Lobby View From Outdoor Classroom Corridor

Discover

CORRIDOR
Wetlands



Interior Concepts | Stair D - Music and Gymnasium Lobby

Each area will feature local nature scenes and celebrate students' differences and the different ways that they learn.

Discover
CORRIDOR
Wetlands

Play, Read,
& Create
MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond

Explore
STAIR A
Local & New England
Trails and Parks

Search
CENTRAL STAIR
Sawmill Brook

Building Interior | Stair D - Music and Gymnasium Lobby

Play, Read,
& Create

MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond




Building Interior | Stair D - Music and Gymnasium Lobby

Play, Read,
& Create
MUSIC, GYMNASIUM,
& STEAM SUITE
Mill Pond



Wall Art Opportunities | Tile Mosaic Wall

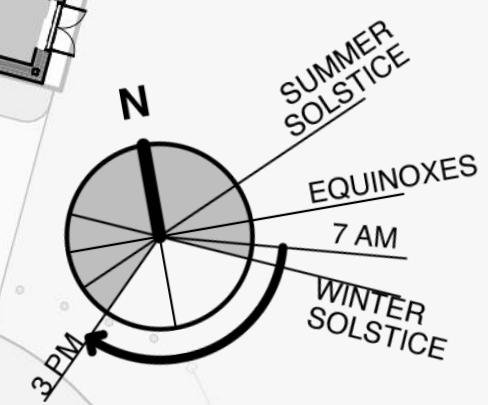

Wall Art Opportunities | Tile Mosaic at Main Lobby



Wall Art Opportunities | Tile Mosaic - Precedent



Hastings Elementary School | Lexington, MA

Building Interior | Cafeteria



Building Interior | Cafeteria



Building Interior | Second Floor Corridor - Media Center Entrance



Building Interior | Media Center



Building Interior | Media Center



Building Interior | Kindergarten Project Area



Building Interior | Typical Classroom Project Area



Building Interior | Typical Classrooms



Next Steps | Meetings + Milestones

Design + Construction Schedule

- Construction Documents - March 2025 to November 2025
- Project Bid - December 2025 through January 2026
- Building Construction April 2026 to February 2028
- Building Completion + Occupancy - February 2028
- Demolish Existing Building + Complete Sitework - March to October 2028

Submissions

- 4/2/25: Planning Board Site Plan Approval Application
- 4/5/25: Conservation Commission Notice of Intent
- 7/18/25: MSBA 60% CD Submission

Upcoming Meetings

- 4/8/25: MSBA Design Status Meeting
- 4/24/25: Conservation Commission Hearing
- 5/15/25: Planning Board Hearing



School Building
Committee
Meeting

BURLINGTON ELEMENTARY SCHOOL

Burlington, MA

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn

SBC Meeting Agenda – April 8th 2025

1. Call to Order & Intro
2. Public Comments (10 Minutes)
3. Approval of the March 18th Meeting Minutes –Vote Expected
4. Invoices and Commitments for Approval – Vote Expected
5. Project Update
6. Other Topics not Reasonably Anticipated 48 hours prior to the meeting
7. Public Comments (10 Minutes)
8. Adjourn
